

Aker BP Prosjektmodell

Smidig og sømløs prosjektgjennomføring

Marie Ravnestad

Prosjektkonferansen 21.09.2023

Record number of field development plans



“(...) a manifestation of our ambition to create the oil and gas company of the future – with low costs, low emissions, profitable growth and attractive returns”

Karl Johnny Hersvik

Our Philosophy & Approach

One Team

HSE

Prioritize **Quality** (front loading) to enable the schedule

Deliver on **Schedule** to enable cost performance

Predictable **Cost** and better margins for our alliances and partners

Return of **Value** to stakeholders and society


SAFER

How we organize our projects

Governance Structure based on Asset Model

Integrating across discipline areas

The risk for rework in the project is reduced by good project integration and good level of maturity across the project disciplines, in combination with a shared understanding of uncertainties and their potential impacts on the project in the project team

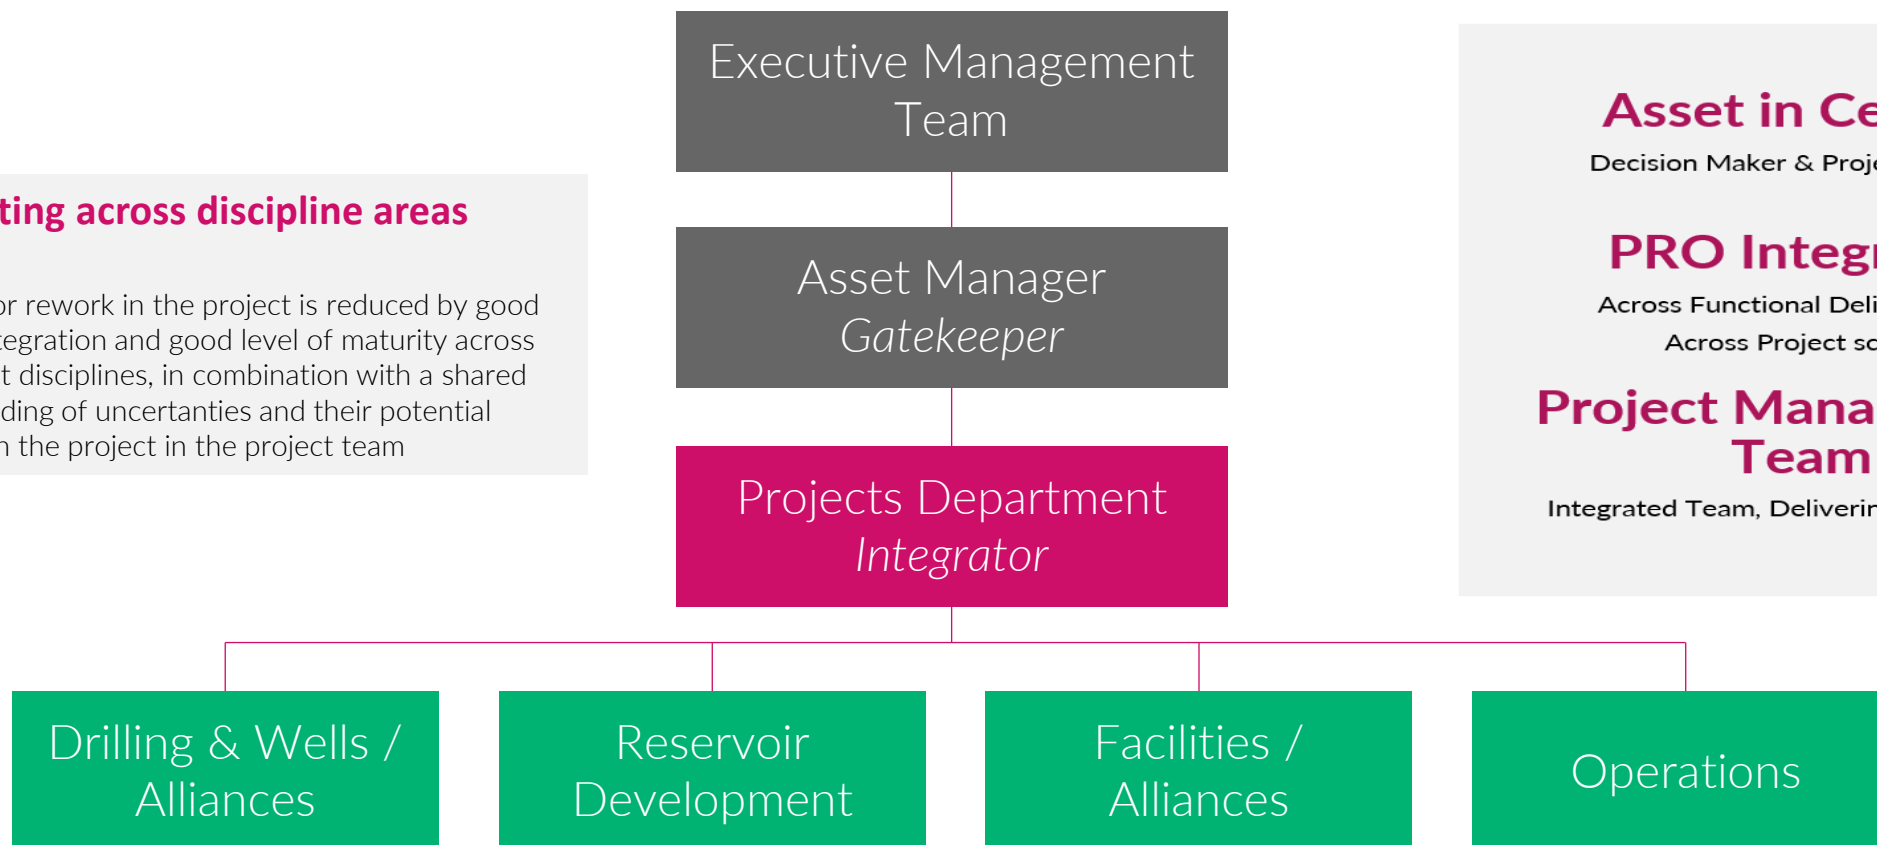

Asset in Center

Decision Maker & Project Owner

PRO Integrator

Across Functional Delivery Lines
Across Project scopes

Project Management Team

Integrated Team, Delivering on Mandate

How we organize our projects


Stage Gate Process

project maturation and execution model

The Project stage Gate Process provides a standardised framework for initiating, maturing and executing projects to ensure delivery of projects aligned with the established mandate and business case.

The process will prove the relevant governance to ensure:

- efficient maturation, planning and execution of the project
- sufficient maturity of the project for it to be presented to the Gate Keeper at the decision gate
- consistent evaluation and decision processes within Aker BP and towards partners, government agencies and other stakeholders
- optimization of the value outtake from project entry to project close out




What is so special about this?


How we organize our projects

Standardized set-up of Project Teams


A standardised and scaleable organisational set-up for individual project delivery and for project portfolio delivery enables us to implement a process for projecting resource demand across project delivery lines.

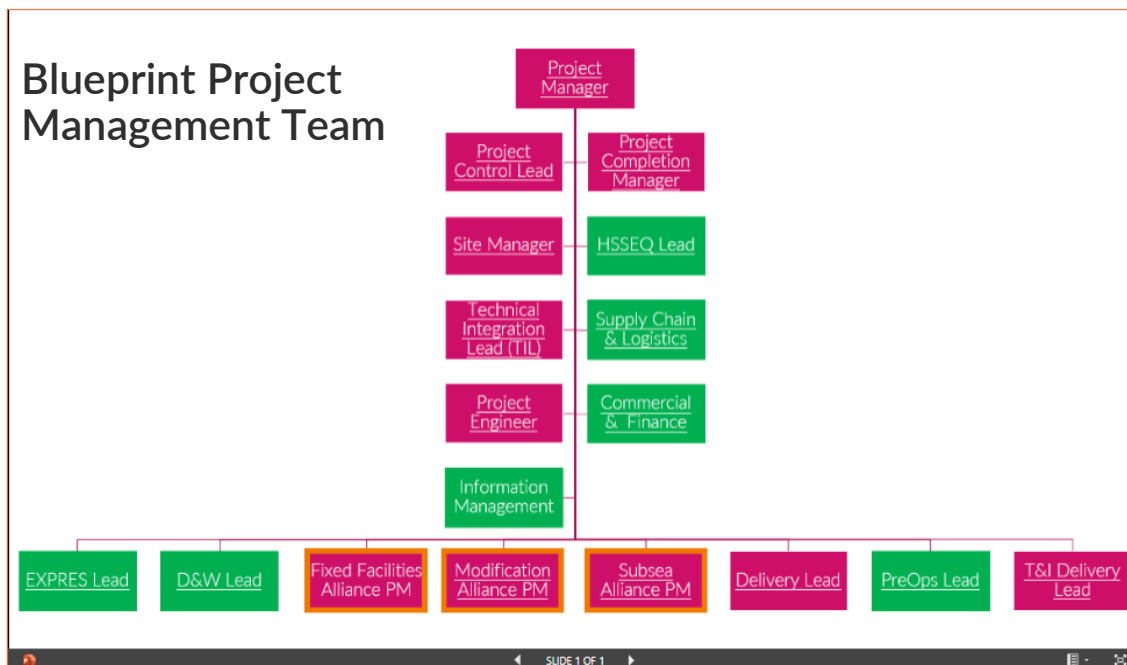

Manpower planning (MPP)

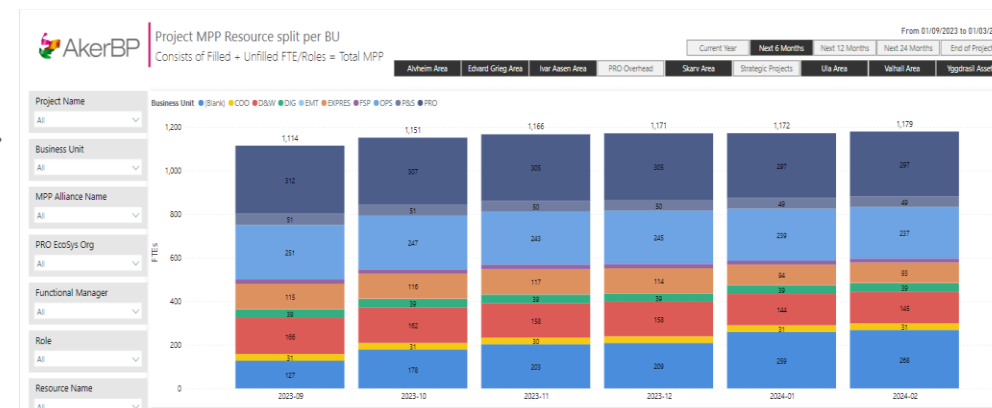

Key principles for successful project execution

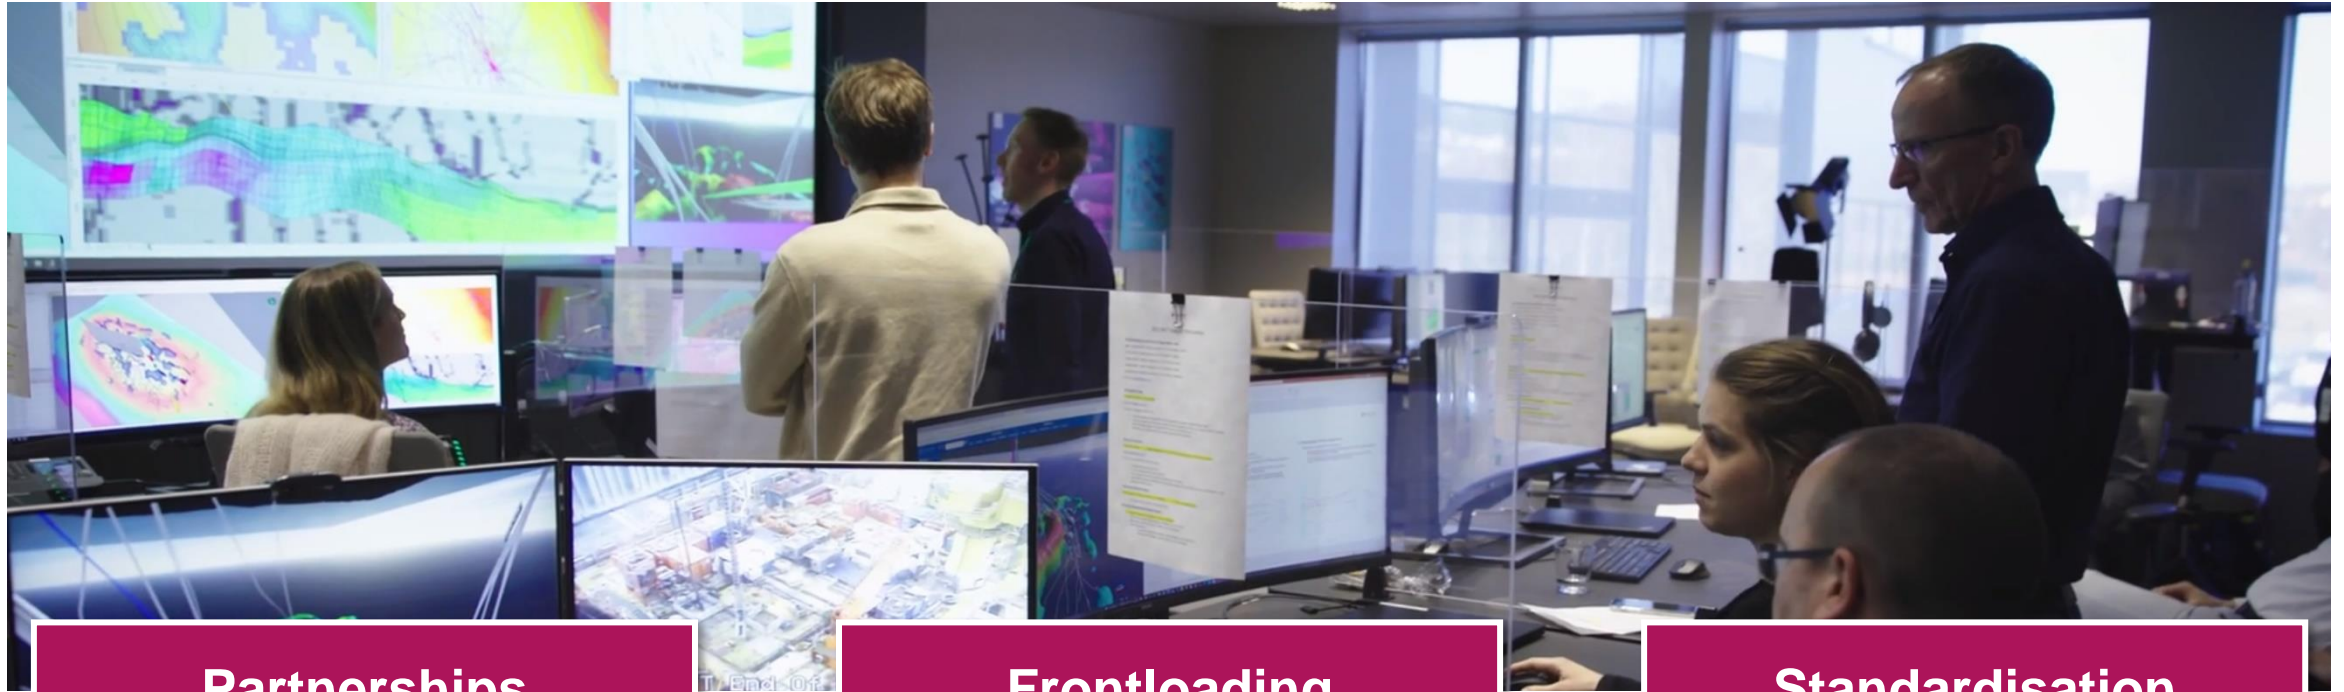

Partnerships

- ✓ Competence and learning
- ✓ Continuity
- ✓ Common goals and shared incentives

Frontloading

- ✓ Early planning and maturation
- ✓ Supplier involvement
- ✓ Secured yard and rig capacity


Standardisation

- ✓ Well designs and equipment
- ✓ Topside and subsea equipment
- ✓ Facilitate efficient operations

How we organize our projects


Delivering Projects as Portfolio

identify synergies and mitigate common risks

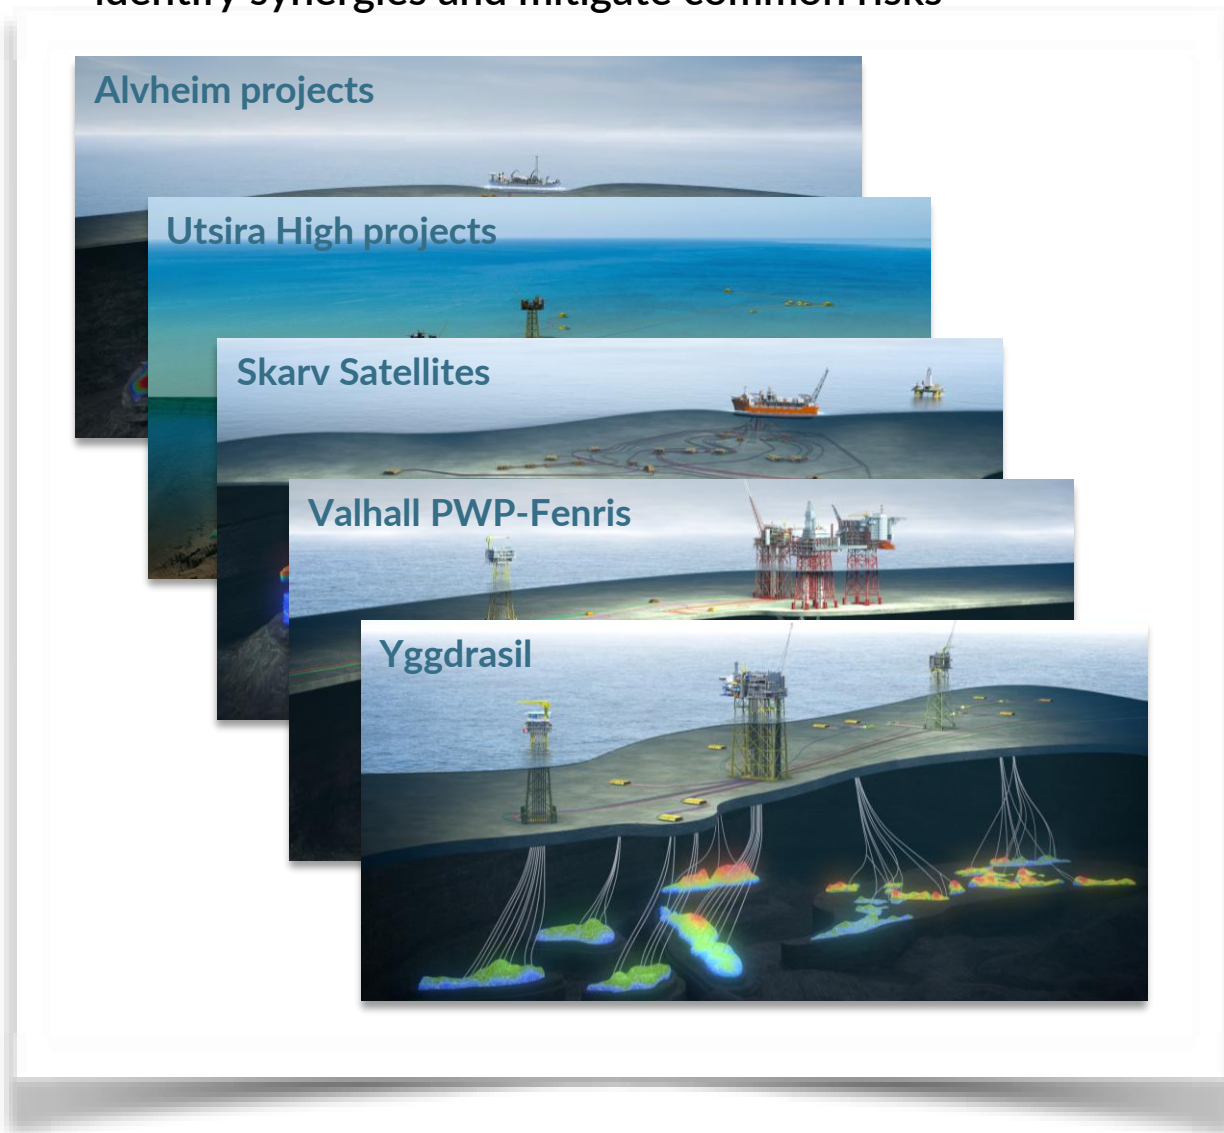


Project Governance Model

accountability and efficient decision making

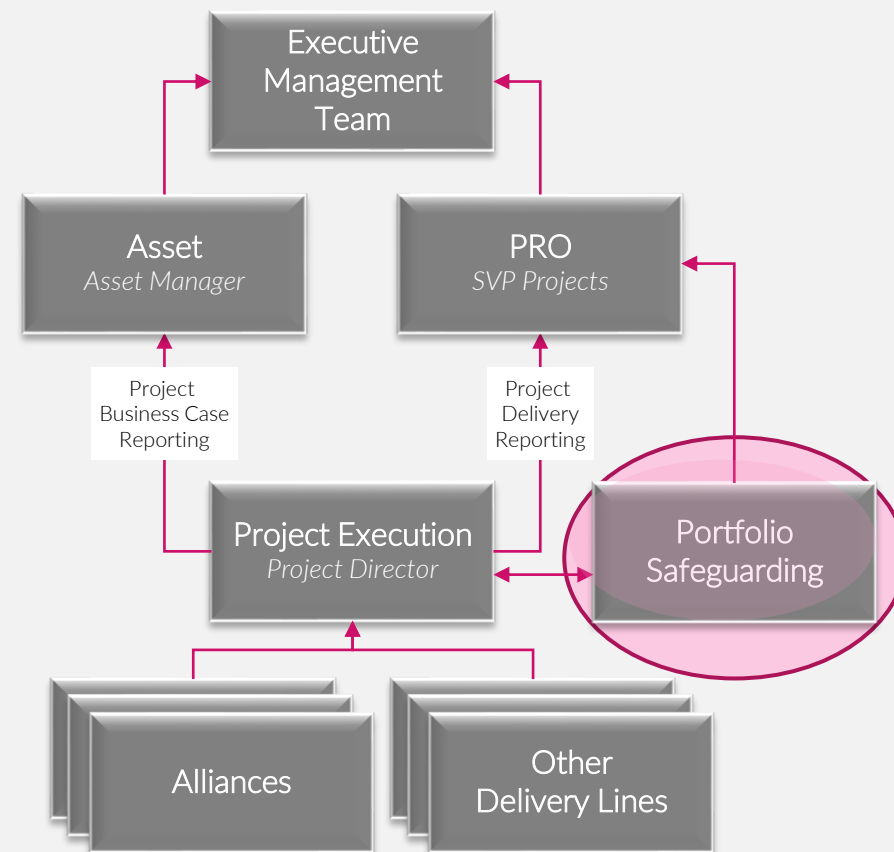

Does Our Delivery Model Work?

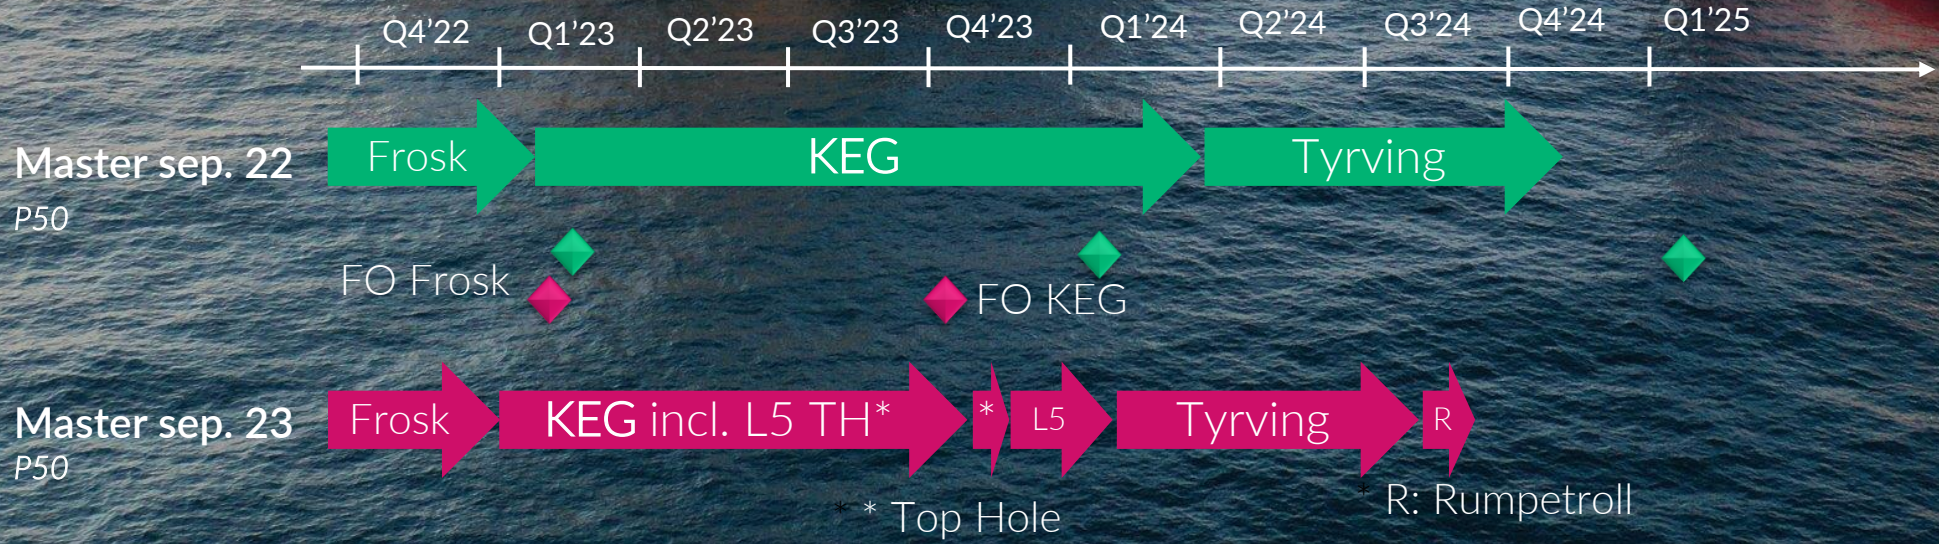



Execution model w collaboration focus

- Improved performance
- Schedule optimization – lower cost & earlier income
- Focus on solving problems together



www.akerbp.com
